



Helix Logistics transformation: steering committee

Every exhibit type of the engine on one fictitious programme

Today we review diagnosis, plan and value, and ask for one decision

01

Diagnosis

Where cost-to-serve comes from

02

Programme

Initiatives, plan and organisation

03

Value and decision

Savings to date and wave 2 funding

Wave 1 is delivering; releasing wave 2 funding keeps the €48M target on track


Situation	Cost-to-serve is 18% above peers	Network and warehouse inefficiencies explain 70% of the gap.
Complication	Wave 1 savings arrive, but automation needs capex now	Hub automation lead times are 9 months; delaying funding pushes €14M of savings into 2028.
Resolution	Release €22M for wave 2 today	Keeps the €48M run-rate target for 2027; payback in 19 months.

01

Diagnosis


Helix's cost-to-serve is 18% above the peer median, the highest of the panel

Cost-to-serve, 2025, index, peer median = 100

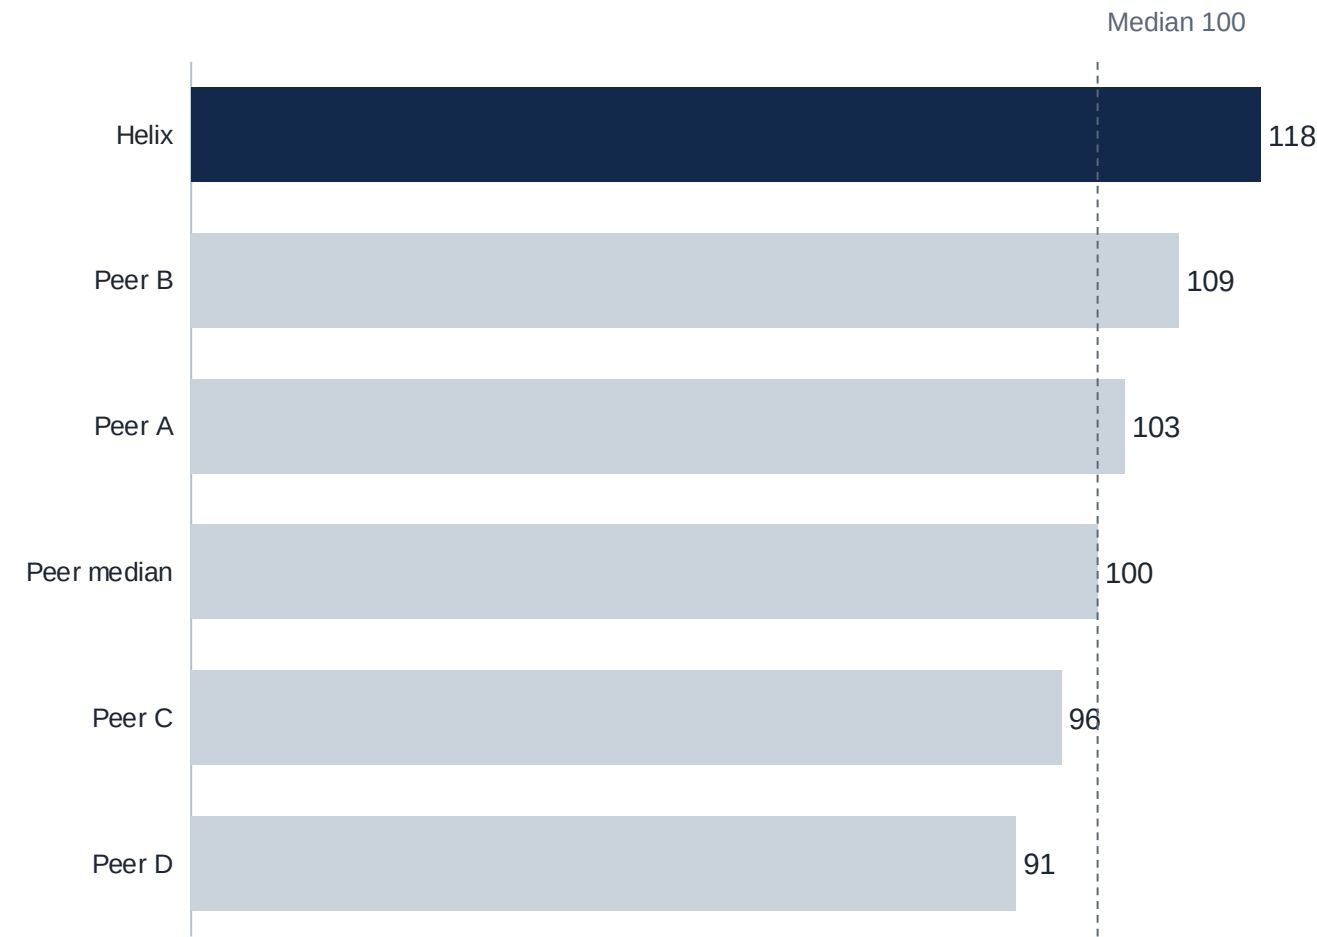


- Helix is **18 points** above the median and 9 above the next worst peer
- The gap widened by 5 points since 2022

Network and warehousing explain €31M of the €44M gap to peers

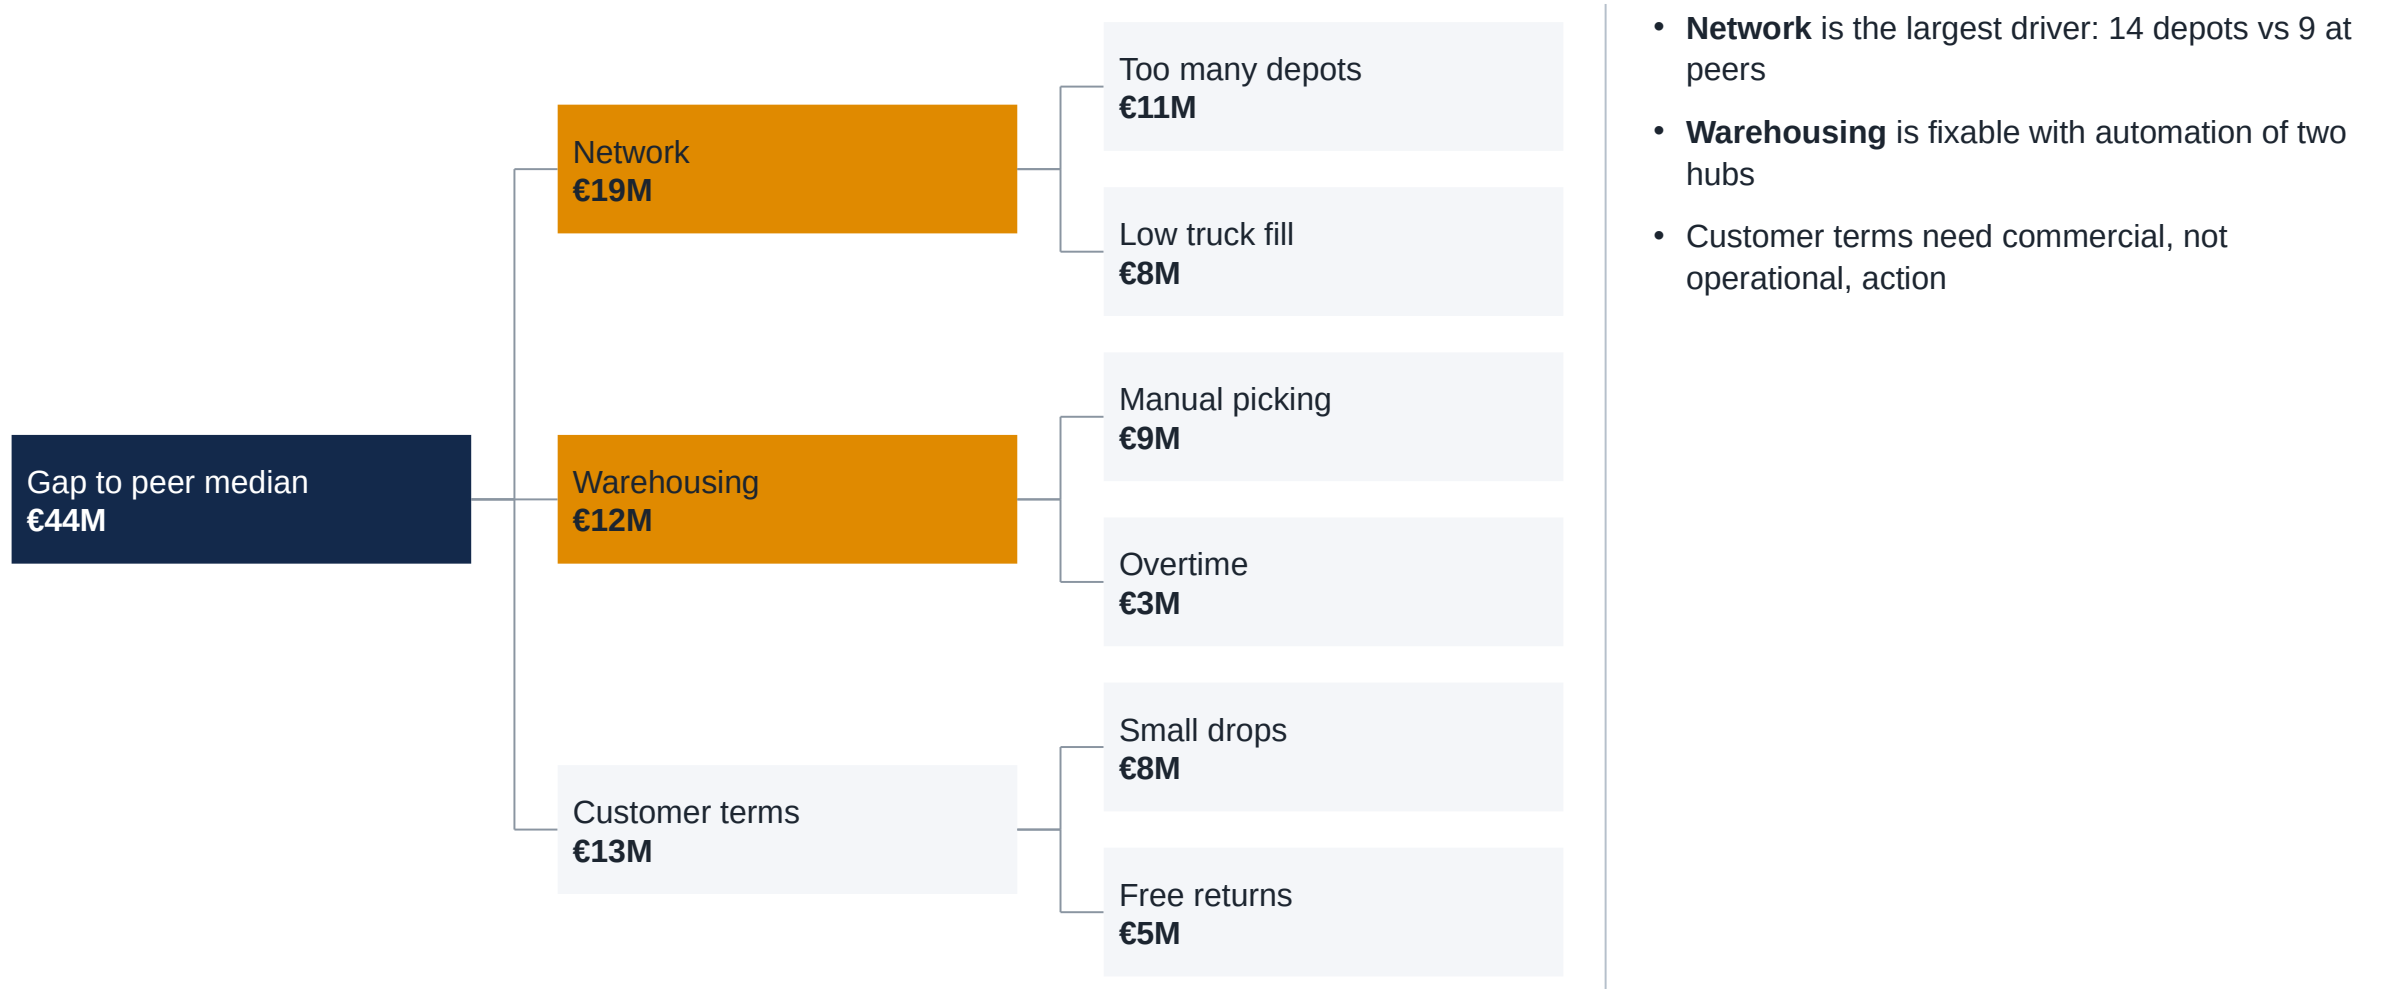

Cost per drop rose 21% since 2021 while peers held it flat


Cost per drop, €

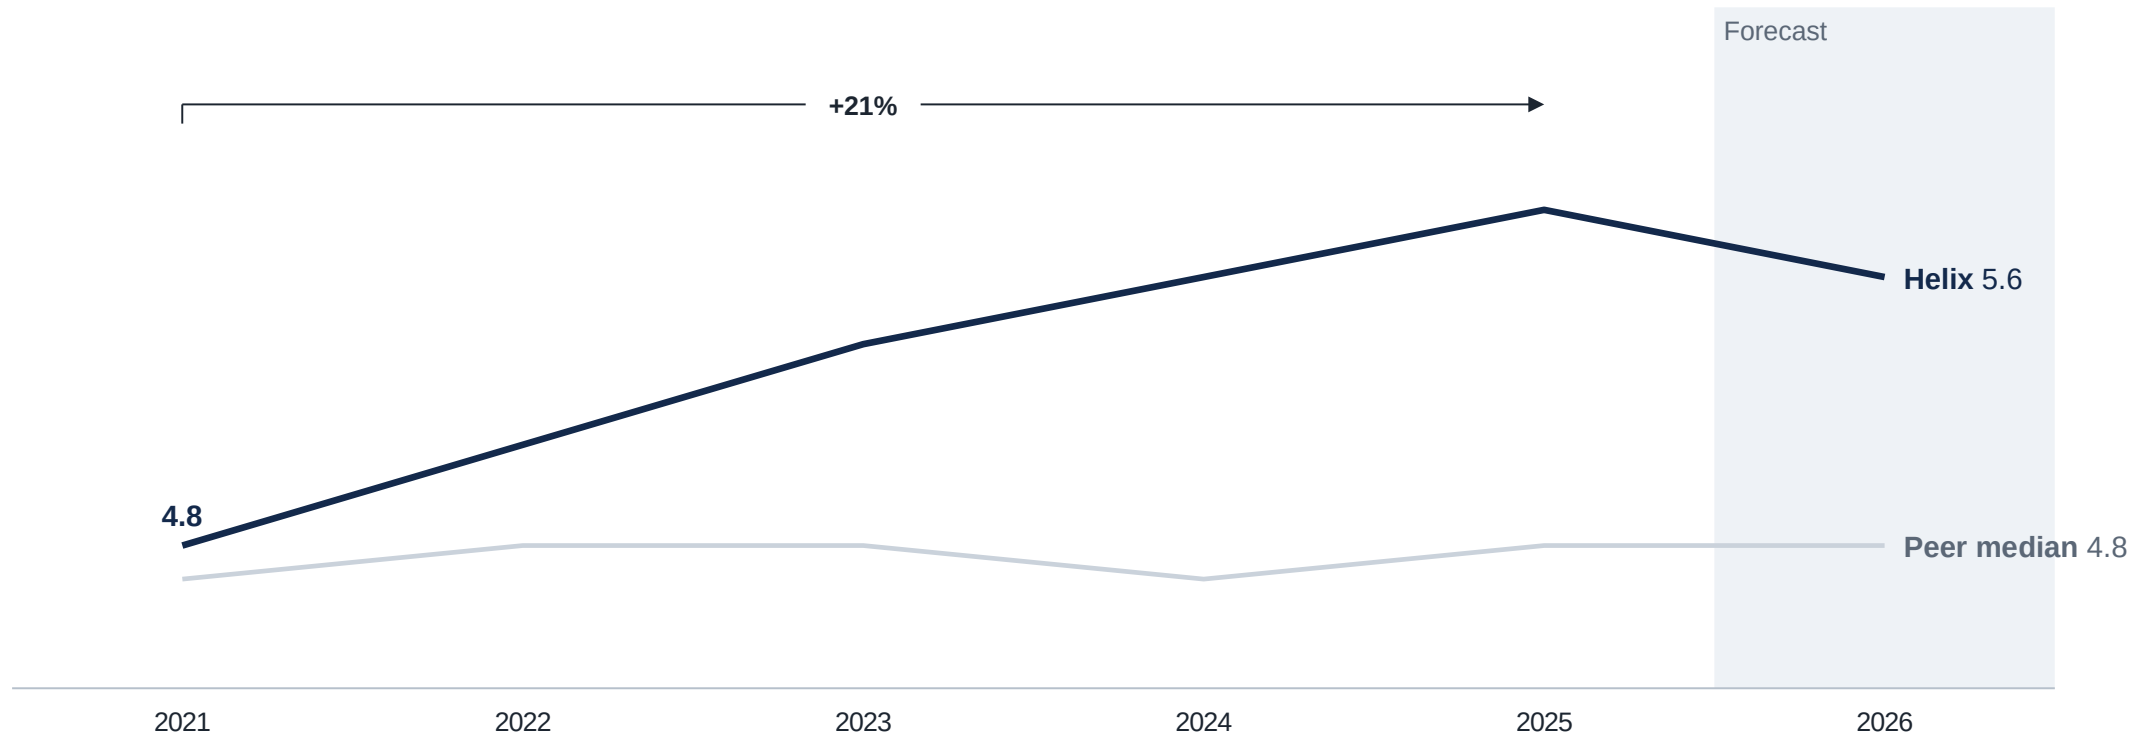

The gap is structural: it grew every year until wave 1 started

Only 61% of orders arrive in full and on time, with picking causing the largest loss


Order fulfilment, Q2 2026, % of orders

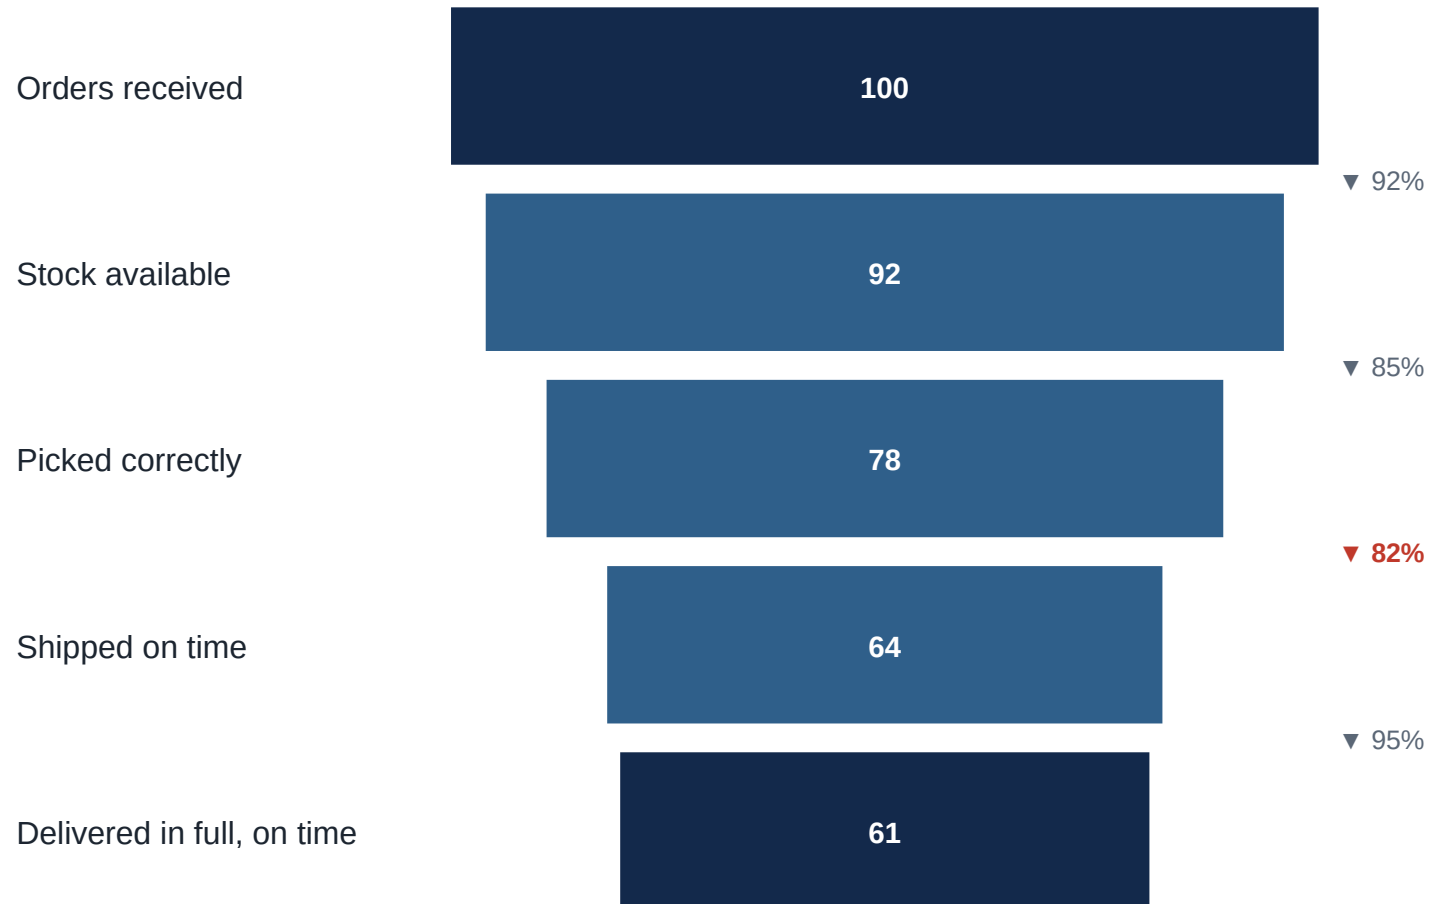

- Picking errors lose **14 points**, the largest single drop
- Stock availability is at peer level (92%)

Cost-to-serve is highest in the north-west, where depot density is lowest

Cost per drop by region, 2025, €

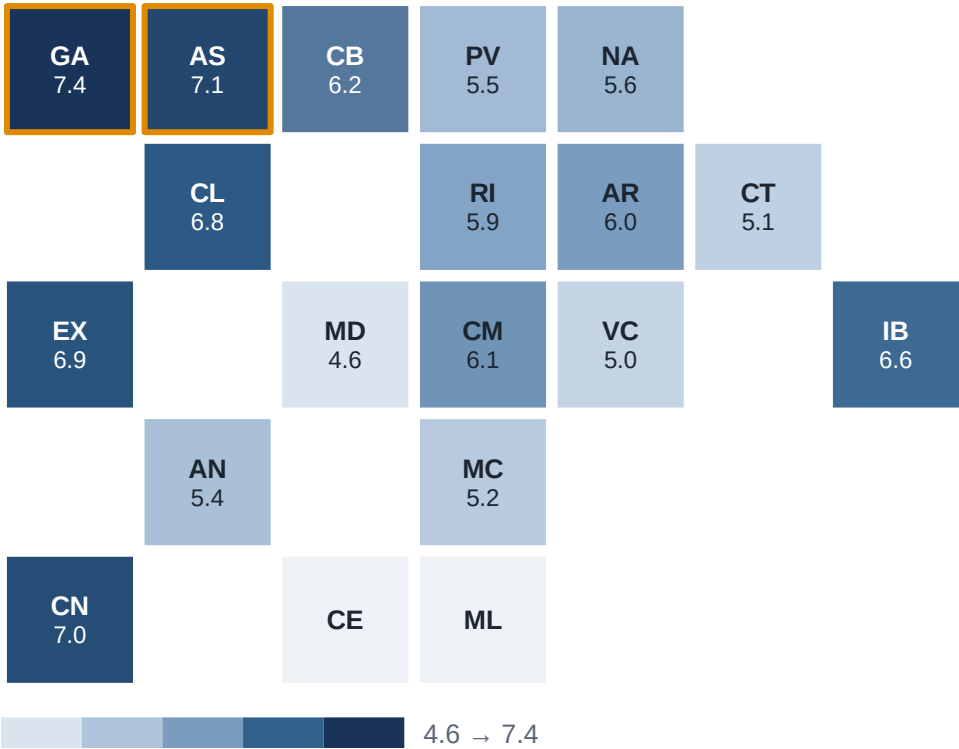


Galicia and Asturias cost **€7+ per drop**, 55% above Madrid

Consolidating three north-west depots saves €6M

Small customers are 38% of drops but only 12% of revenue

Mix by customer size, 2025, % of total

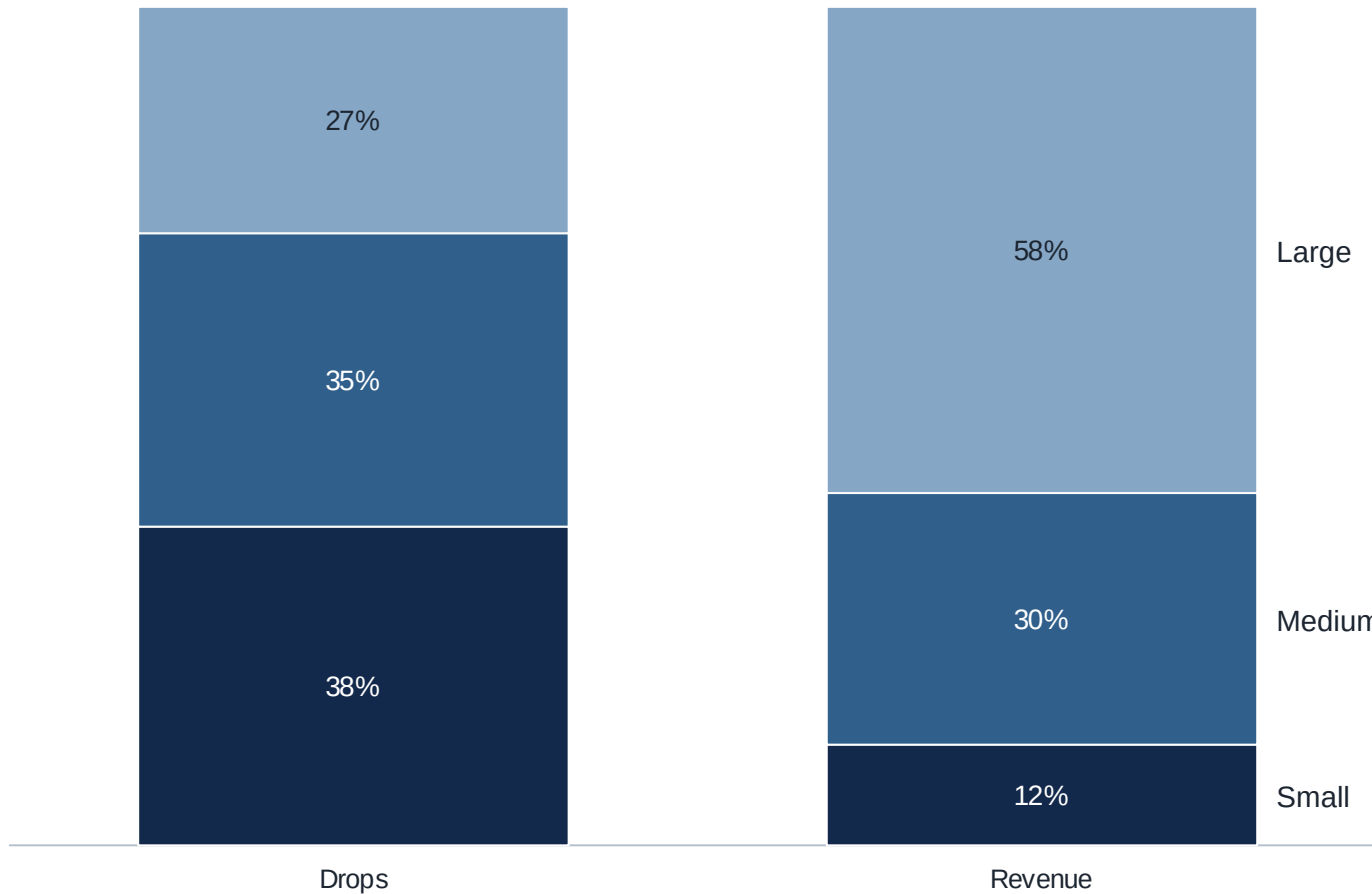


- Minimum order values would remove 20% of drops
- Large accounts subsidise the small ones today

Depots with fewer than 400 drops a day cost up to 40% more per drop

- Below **400 drops a day** fixed costs dominate
- Lugo and Oviedo are candidates for consolidation

Depot volume vs cost per drop, 2025

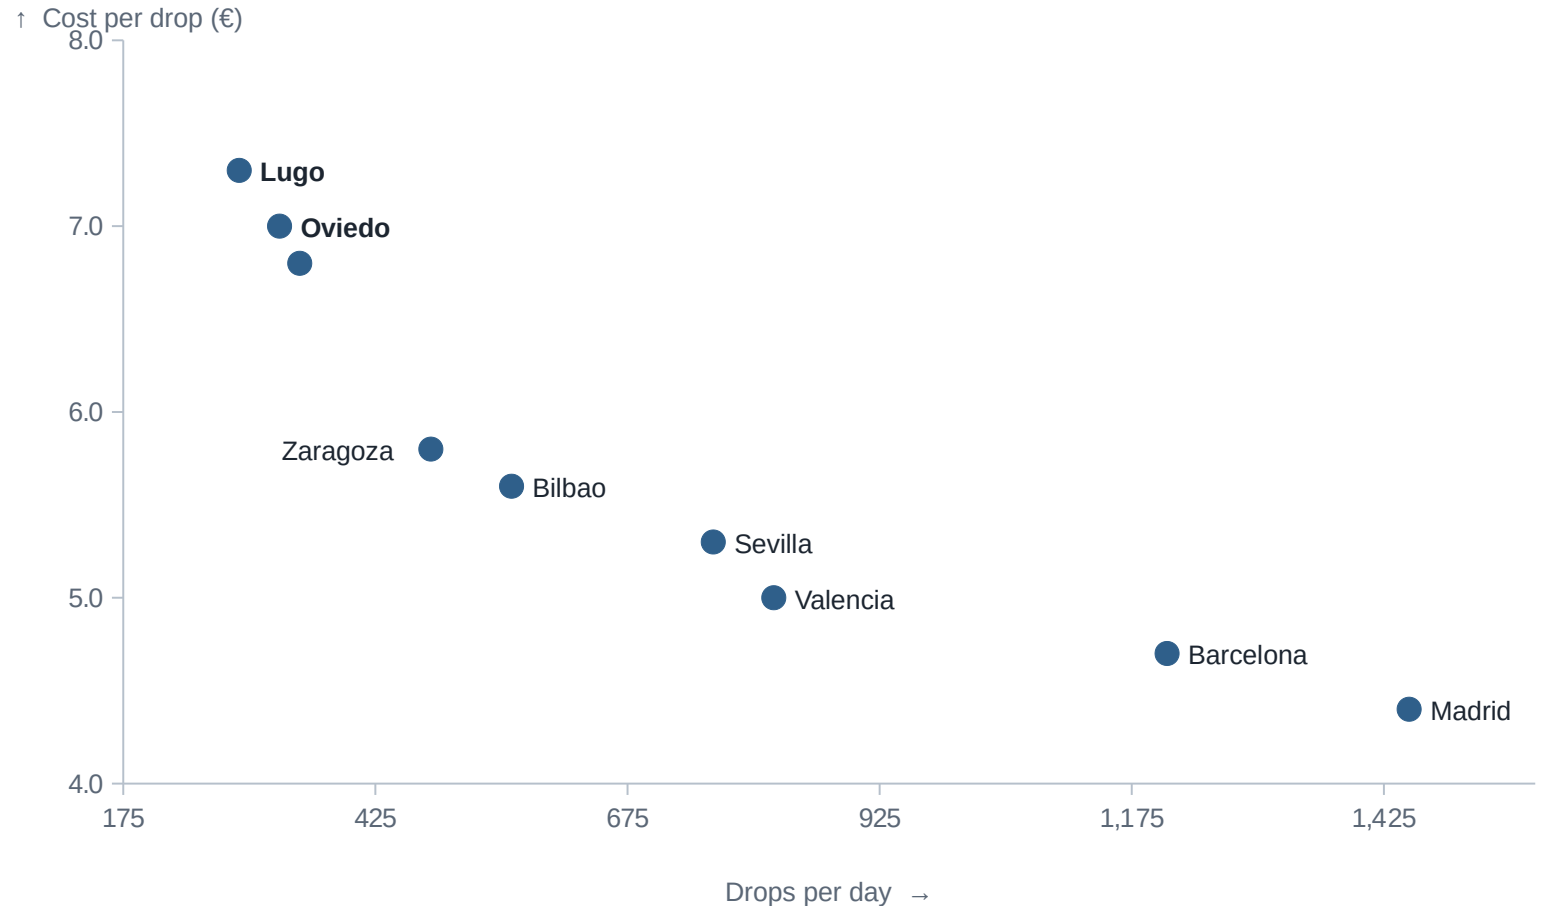

02

Programme

Network redesign and hub automation offer the best value for effort


Initiative assessment

Initiative	Value	Speed	Feasibility	Risk (low = full)	Savings (€M)
Network redesign					17
Hub automation					13
Customer terms reset					11
Transport procurement					7

None Partial Full

Launch terms and procurement first for speed; network and automation carry the value

The new order-to-delivery process removes two hand-offs and the manual picking step

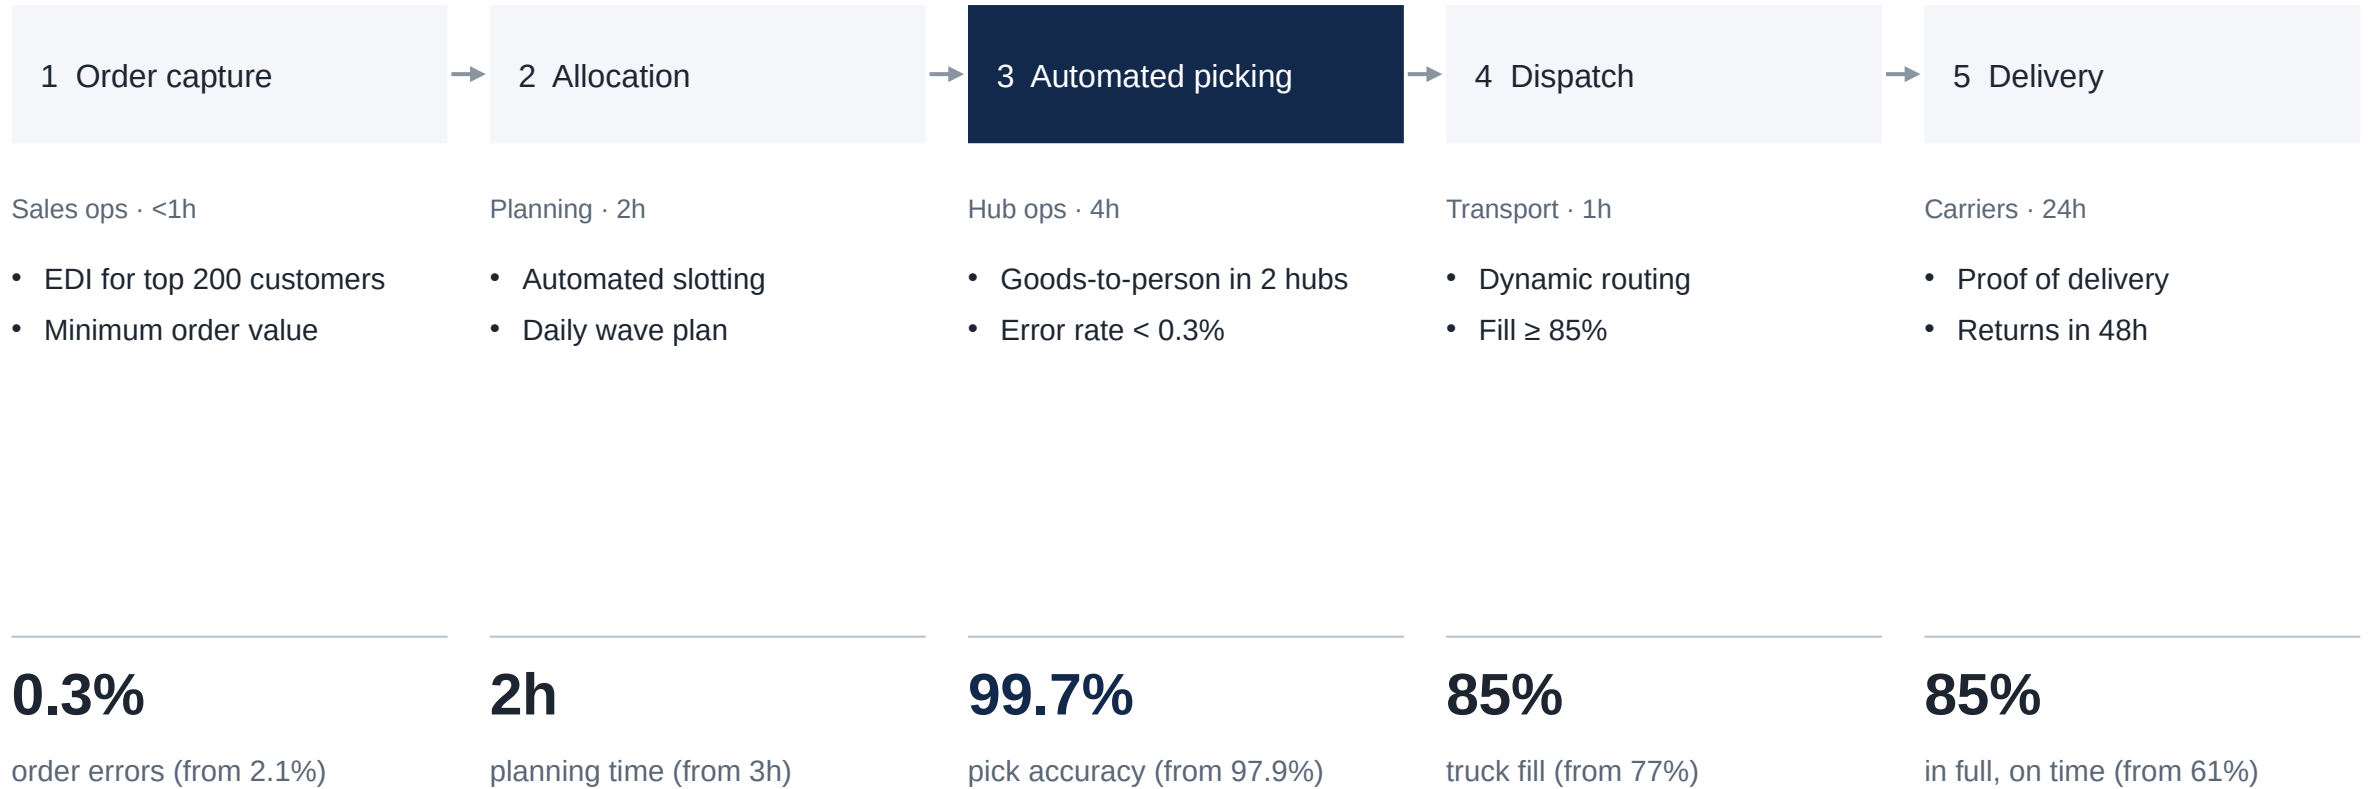


Order-to-delivery falls from 31 to 24 hours and in-full-on-time deliveries rise from 61% to 85%


Customers lose most time at order confirmation and delivery booking



A lean transformation office with four initiative owners runs the programme

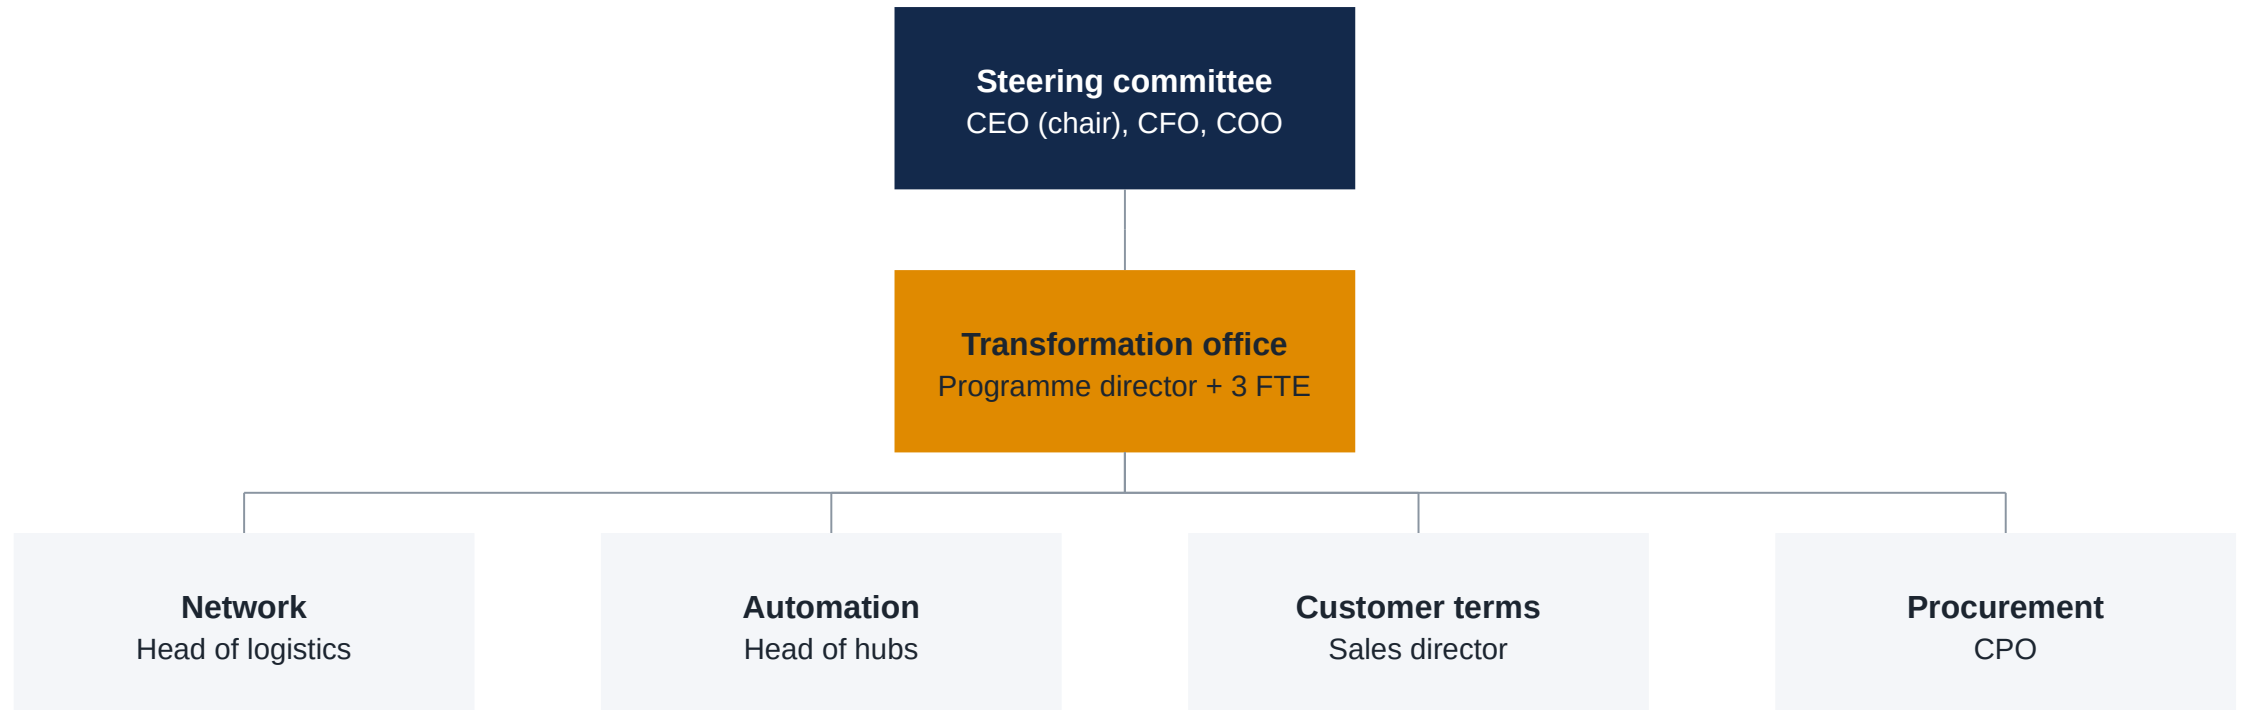

The target architecture adds a WMS and a routing engine on a common data layer

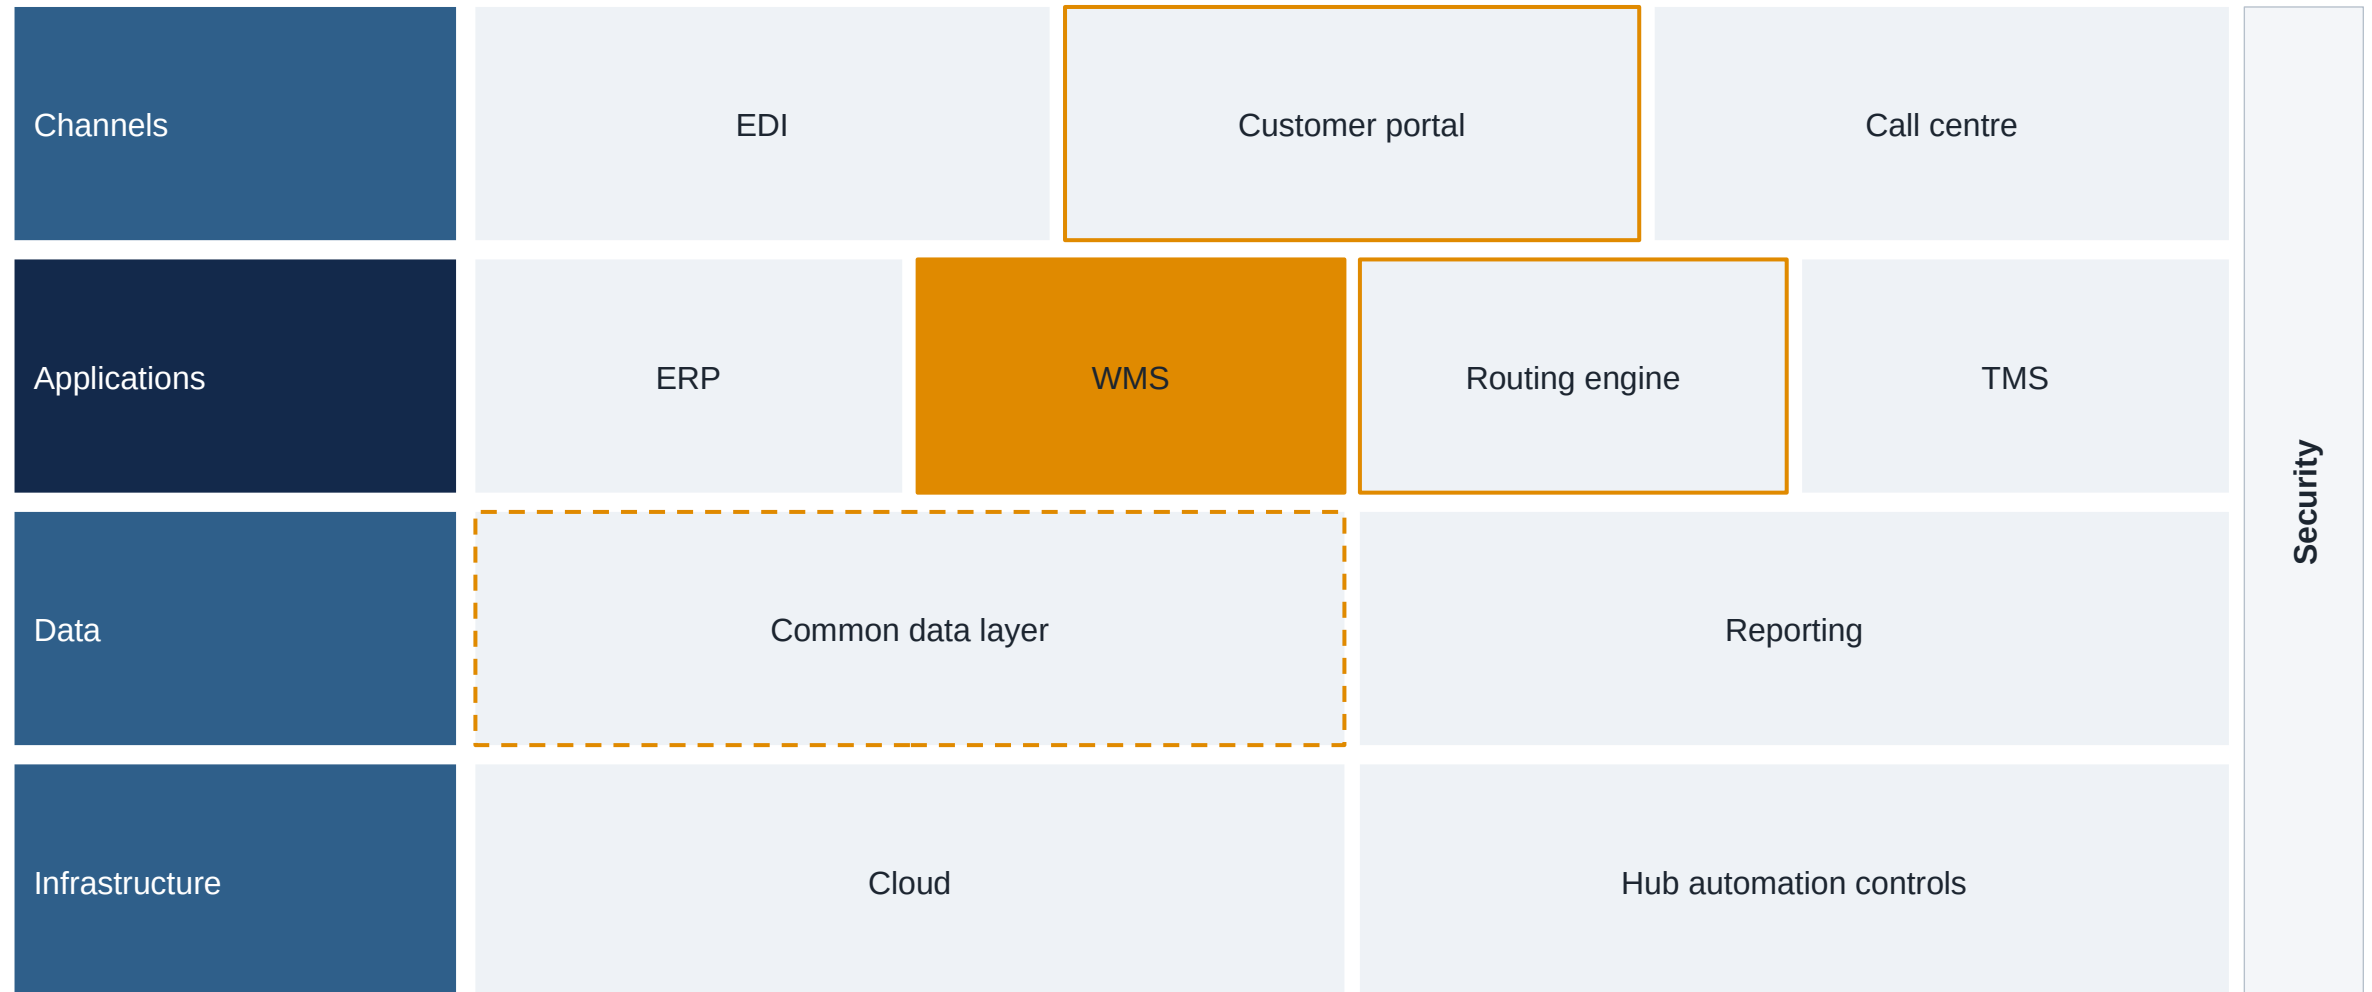

Three phases move from quick wins to structural change within 24 months

Phase 1 · Quick wins

€11M

run-rate by Q4 2026

Fund the programme

- Customer terms reset
- Transport tender
- Overtime controls
- Self-funding by Q4 2026

Phase 2 · Automation

€13M

run-rate by Q3 2027

Fix the hubs

- Goods-to-person in 2 hubs
- WMS go-live
- Pick accuracy > 99.7%
- Capex €22M, payback 19 months

Phase 3 · Network

€17M


run-rate by Q4 2027

Redesign the network

- Close 5 depots
- Two new cross-docks
- Dynamic routing
- Needs works-council agreement

Phase 1 savings fund phase 2, and phases 1-2 de-risk the network redesign before any depot closes

Five milestones gate the programme; the WMS go-live in Q2 2027 is the critical one

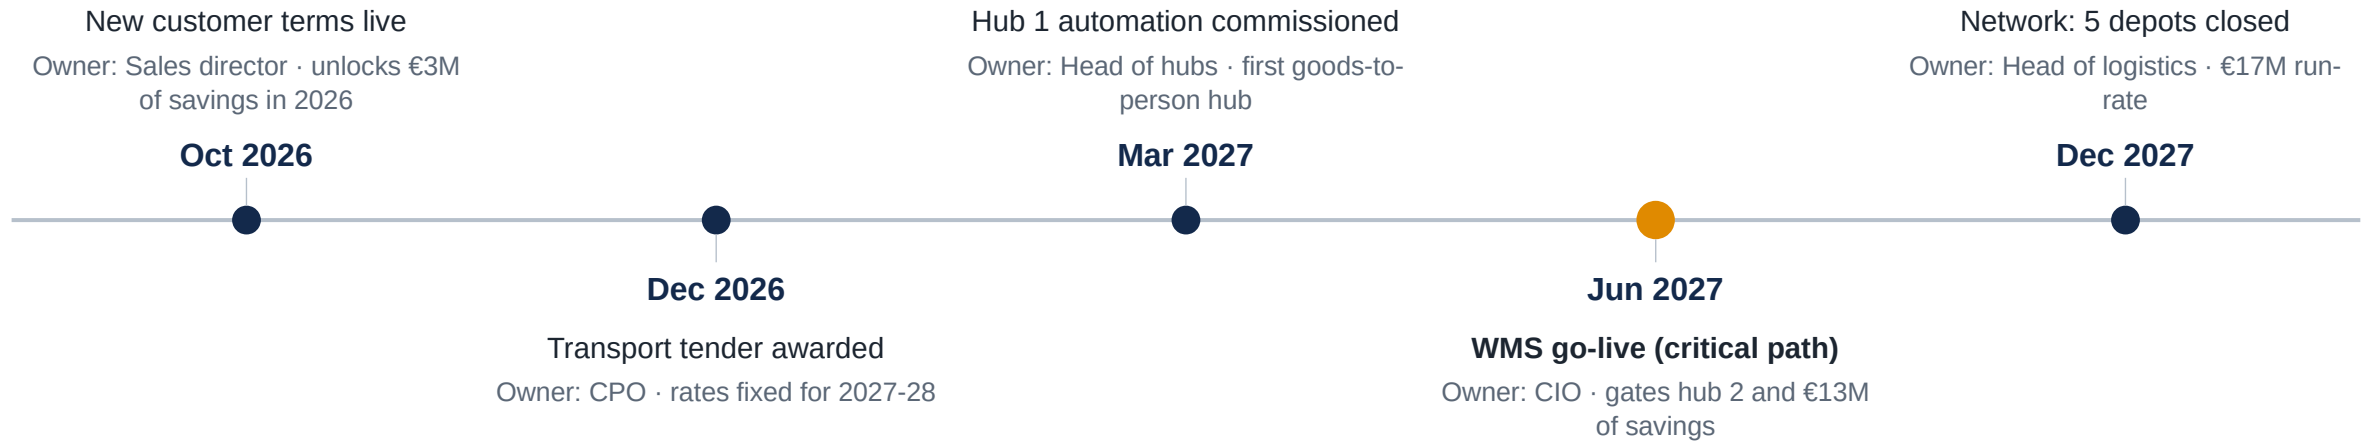

Why June 2027 matters

The **WMS go-live** gates hub automation and €13M of savings

A one-quarter slip defers **€3.5M** of run-rate savings

Mitigation: parallel data migration and a frozen scope from Q4 2026

03

Value and decision

Three of four initiatives are on track; automation is amber on supplier lead times

Initiative status, September 2026

Initiative	Owner	Savings to date (€M)	Target 2027 (€M)	Status	Comment
Customer terms reset	Sales director	3.2	11		Signed with 60% of accounts
Transport procurement	CPO	2.1	7		Tender closes in December
Hub automation	Head of hubs	0.0	13		Supplier lead time +6 weeks
Network redesign	Head of logistics	0.4	17		Works council consulted
Total		5.7	48		

Wave 1 already cut cost per drop by 3% and overtime by a fifth

€5.7M

▲ **+€2.3M vs plan**

Savings delivered to date

Mostly customer terms and transport rates

€5.63

▼ **-3.0% vs 2025**

Cost per drop, August

First decline in five years

81%

▲ **+4pp**

Truck fill

Dynamic routing pilot in Madrid

-21%


▼ **-21% YoY**

Overtime hours

New shift patterns in 3 hubs

€48M run-rate savings by 2027, with €24M secured by wave 1 and 2

Run-rate savings build-up, €M

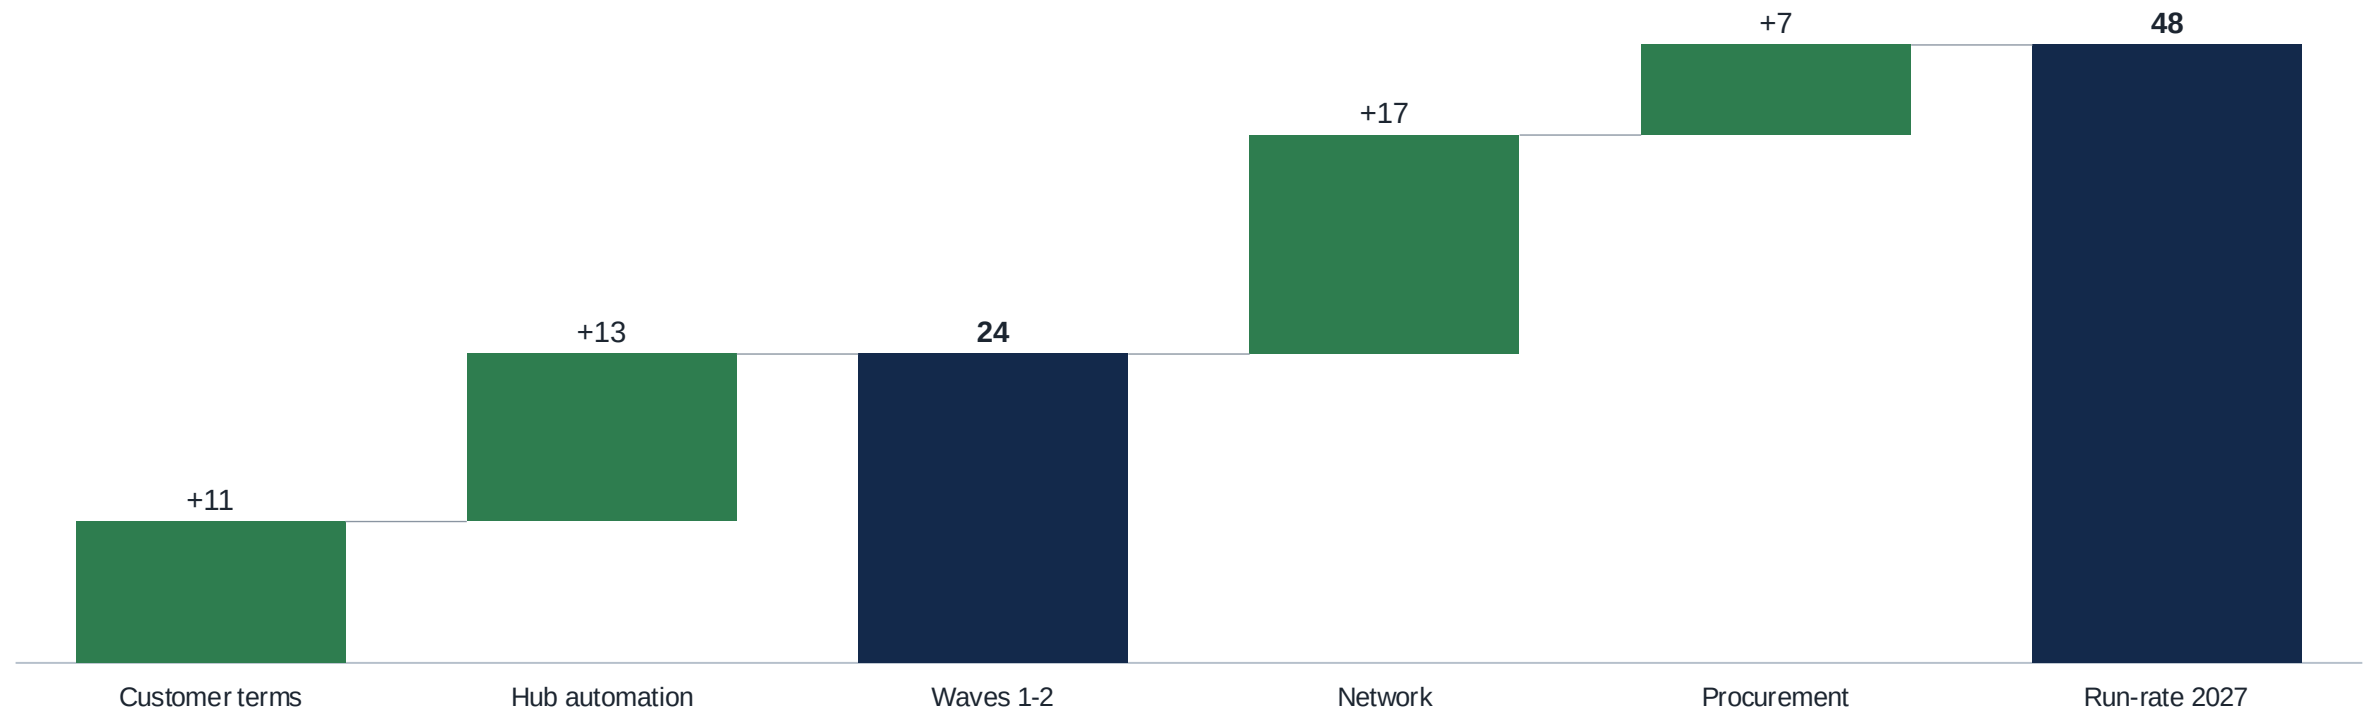


Waves 1-2 secure **half** of the target


Network carries the largest single block and the most execution risk

Savings ramp up in every initiative, with automation back-loaded to 2027


Customer terms, €M

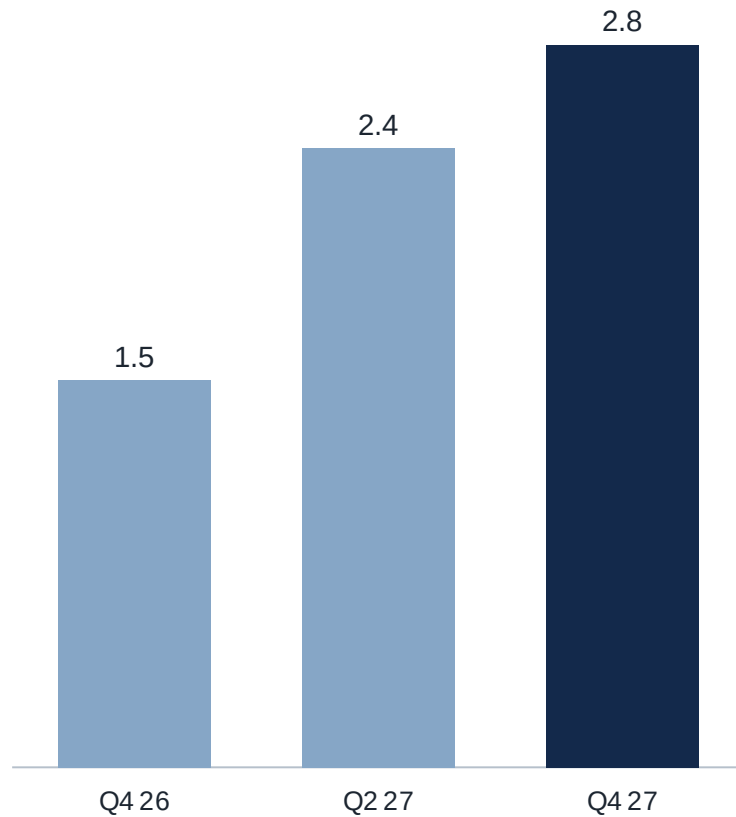

Hub automation, €M

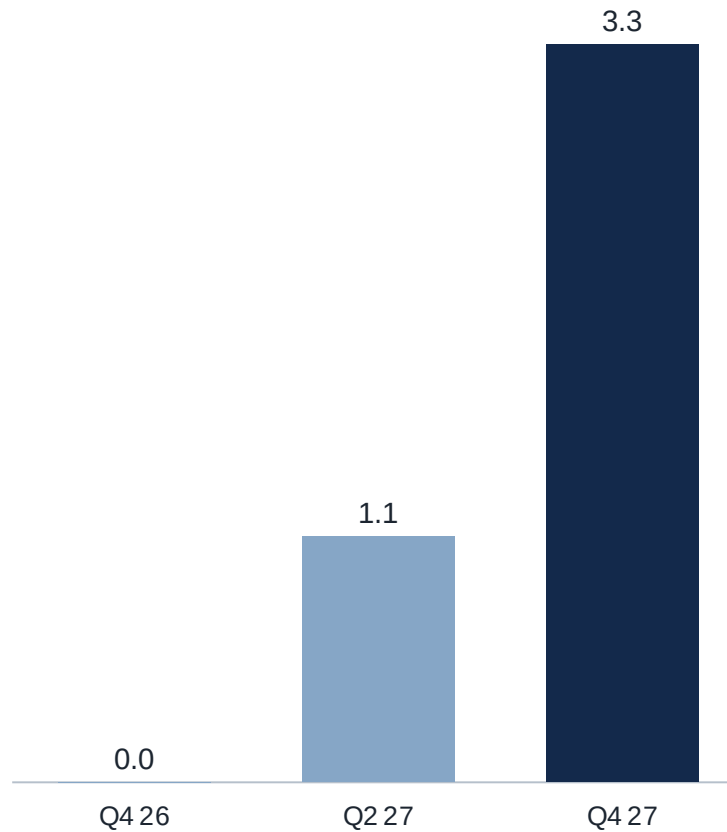


Network, €M

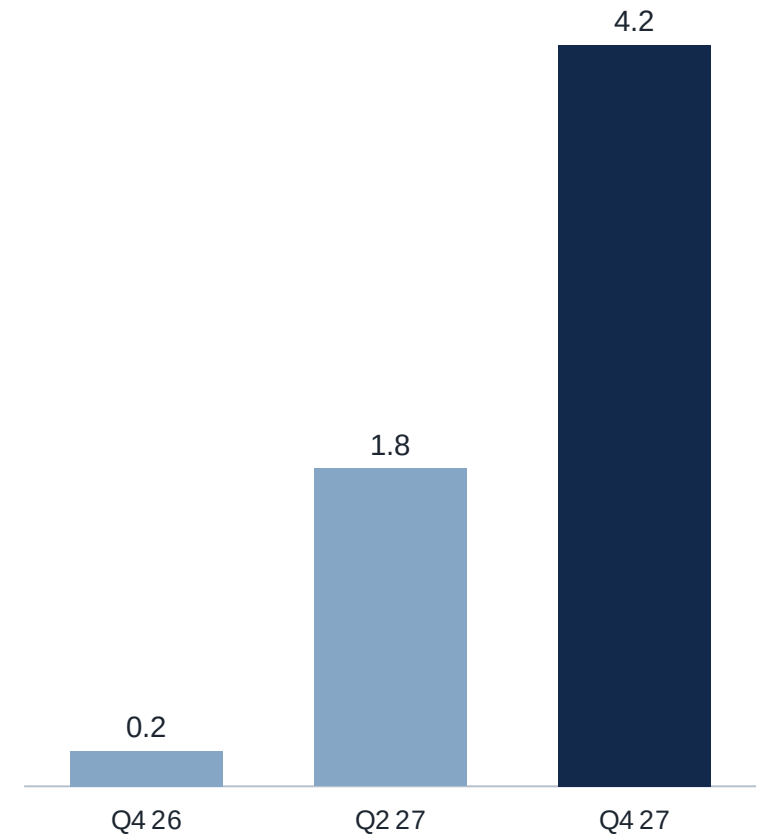

Network and automation deliver 63% of the savings

- Two initiatives carry two thirds of the value
- Both depend on capex released today

Run-rate savings by initiative, 2027, €M

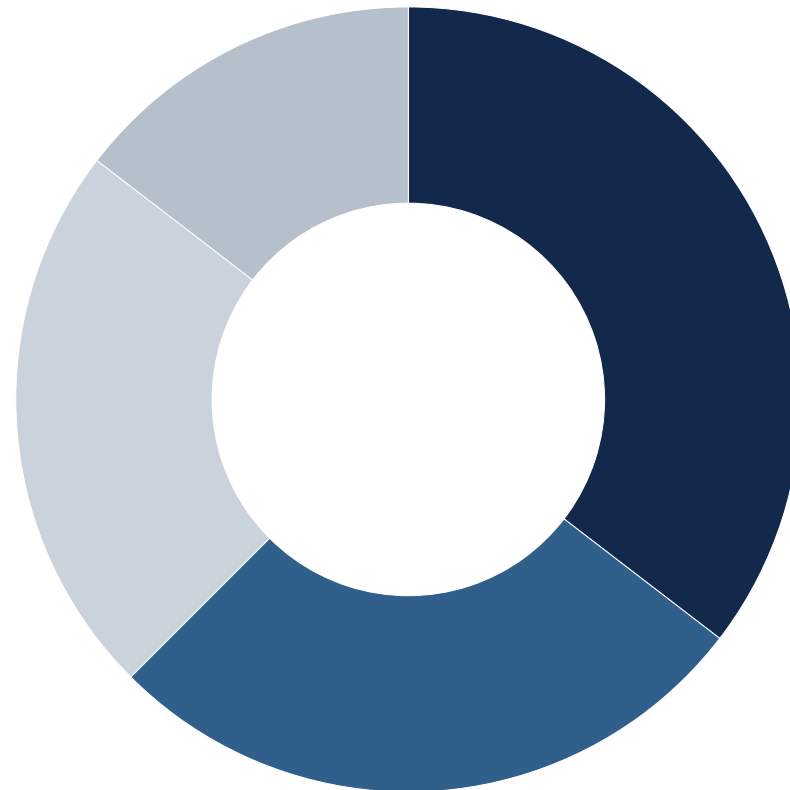

35%	Network (17)
27%	Hub automation (13)
23%	Customer terms (11)
15%	Procurement (7)

Top 2: 62%

Decision requested



**Release €22M of wave 2 funding today to keep the
€48M run-rate target for 2027**

Payback in 19 months; each quarter of delay defers about €3.5M of savings.
